


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		<b>1 Concept Phase &amp; Civil Engineering</b>	<b>91 days?</b>	<b>Mon 5/1/23</b>	<b>Mon 9/4/23</b>	
2		1.1 Geotech Investigator	44 days	Tue 8/1/23	Fri 9/29/23	5
3		1.2 Survey	22 days	Mon 5/1/23	Tue 5/30/23	
4		1.3 Site Plan	66 days	Wed 5/31/23	Wed 8/30/23	
5		1.3.1 Create Site Plan	144 days	Wed 5/31/23	Mon 7/31/23	3
6		1.3.2 Storm Water Plan	22 days	Tue 8/1/23	Wed 8/30/23	5
7		1.3.3 Landscape Plan	22 days	Tue 8/1/23	Wed 8/30/23	5
8		1.3.4 Traffic Impact St	5 days	Tue 8/1/23	Mon 8/7/23	5
9		1.3.5 Lighting Plan	22 days	Tue 8/1/23	Wed 8/30/23	5
10		1.3.6 Concurrency	5 days	Tue 8/1/23	Mon 8/7/23	5
11		1.4 Civil Engineering	22 days	Mon 10/2/23	Tue 10/31/23	4,2
12		1.5 Utility Engineering	22 days	Thu 8/31/23	Fri 9/29/23	4
13		1.6 eVTOL/Heliport Plan	22 days	Tue 8/1/23	Wed 8/30/23	5
14		1.7 Architectural Plan	47 days	Wed 5/31/23	Thu 8/3/23	3
15		1.7.1 Programming	10 days	Wed 5/31/23	Tue 6/13/23	
16		1.7.2 Test Fits	15 days	Wed 6/14/23	Tue 7/4/23	15
17		1.7.3 Concept Design	22 days	Wed 7/5/23	Thu 8/3/23	16
18		1.8 Permitting	176 days	Tue 8/1/23	Tue 4/2/24	
19		1.8.1 FAA Env Review	88 days	Tue 8/1/23	Thu 11/30/23	5
20		1.8.2 SJRWMD ERP Re	88 days	Wed 11/1/23	Fri 3/1/24	4,11,12
21		1.8.3 FAA Heliport Concept Review	66 days	Thu 8/31/23	Thu 11/30/23	13
22		1.8.4 FAA Airspace Rev	44 days	Fri 12/1/23	Wed 1/31/24	12,13,14,19,21
23		1.8.5 FDEP Review of \	44 days	Mon 10/2/23	Thu 11/30/23	12
24		1.8.6 Brevard County Site Plan Review	88 days	Fri 12/1/23	Tue 4/2/24	11,12,13,19
25						
26		2 Architectural Design	132 days	Fri 8/4/23	Mon 2/5/24	14

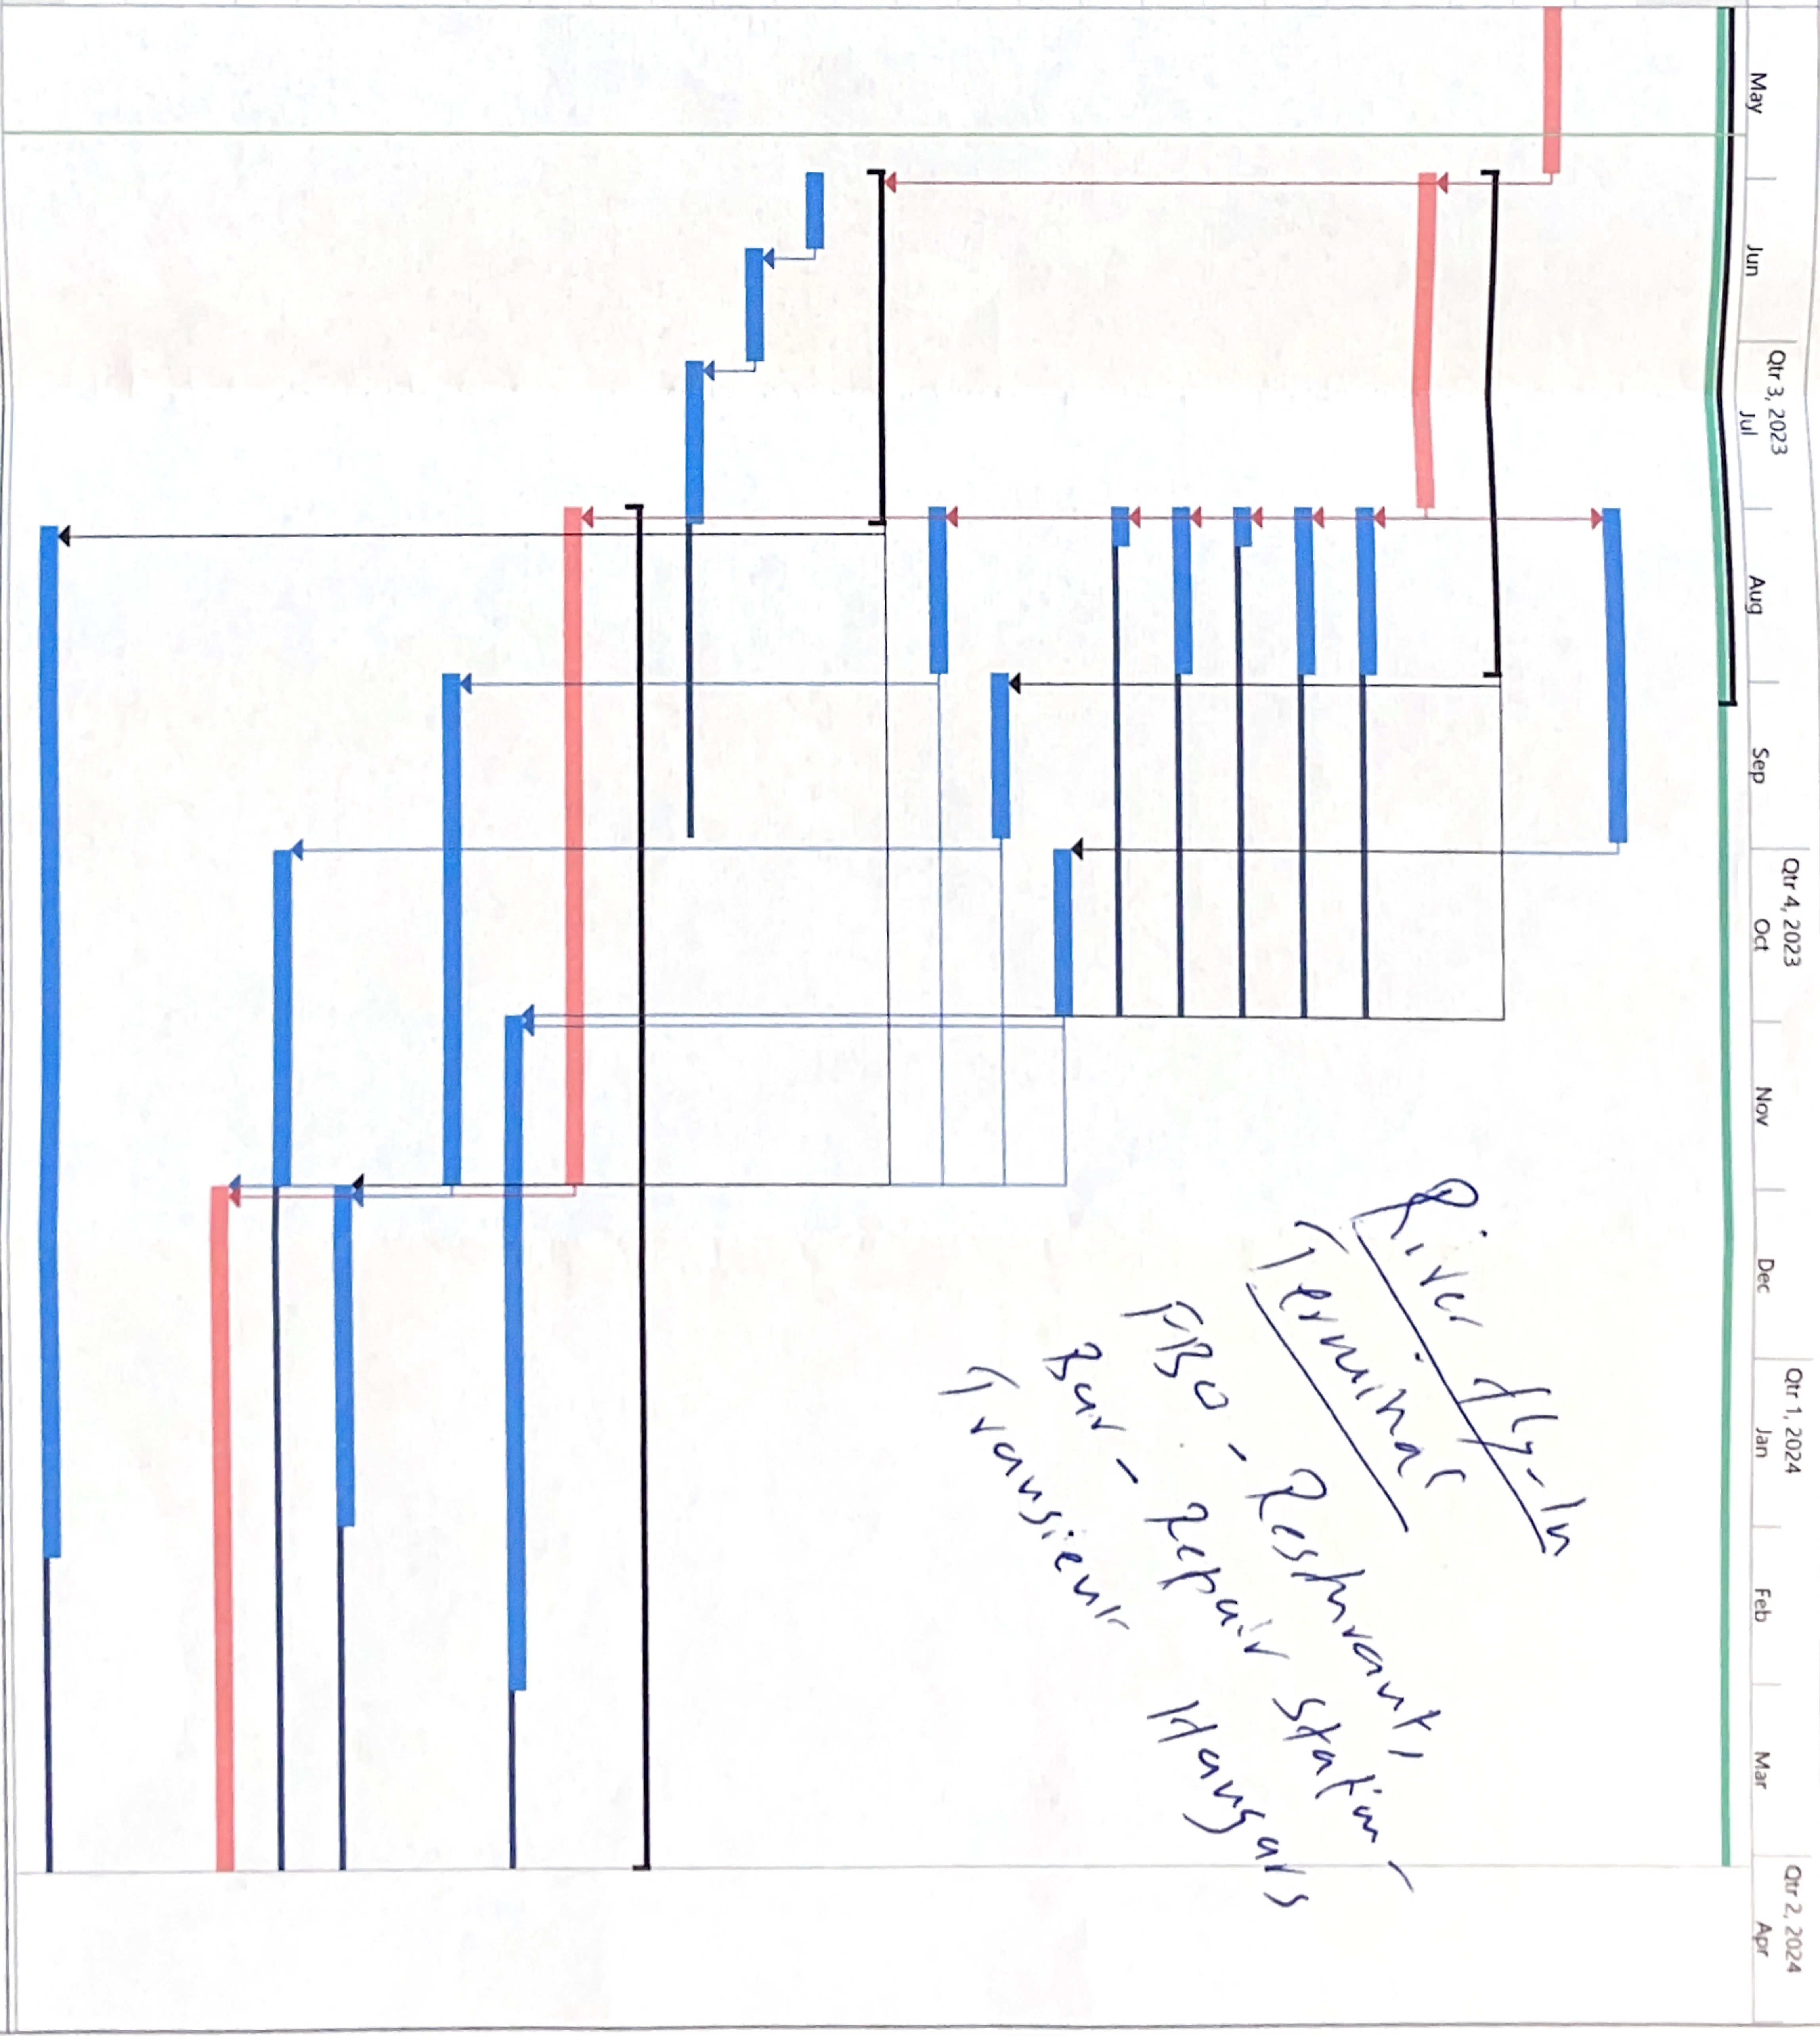

Project: Project Schedule  
Date: Wed 5/24/23

Task Summary: Project Summary, Inactive Task, Inactive Milestone, Inactive Summary

Manual Task Summary: Manual Task, Duration-only, Manual Summary Rollup, External Milestone, Deadline, Manual Progress

Task Legend: Task, Split, Milestone, Summary
